


HAMPTONS WEST Stack 14 - Gantt Chart 07-06-2015

ID	Task Name	Duration	Start	Finish	Predecessors
1	<b>Stack No. 14</b>	<b>62 days</b>	<b>Mon 6/22/15</b>	<b>Tue 9/15/15</b>	
2	<b>Drop #1 (small balcony)</b>	<b>29 days</b>	<b>Mon 6/22/15</b>	<b>Thu 7/30/15</b>	
3	Install Ballustrades	20 days	Mon 6/22/15	Fri 7/17/15	
4	Stucco Application	5 days	Mon 7/20/15	Fri 7/24/15	3
5	Dustwall repairs @ Unit #814	3 days	Thu 7/16/15	Mon 7/20/15	14
6	Spot Prime & Paint	2 days	Mon 7/27/15	Tue 7/28/15	4
7	Remove Swing Stage	2 days	Wed 7/29/15	Thu 7/30/15	6
8					
9	<b>Drops #2 &amp; #3 (large balcony)</b>	<b>62 days</b>	<b>Mon 6/22/15</b>	<b>Tue 9/15/15</b>	
10	Demo: Concrete Columns (6)	5 days	Mon 6/22/15	Fri 6/26/15	
11	Pour: Concrete Columns (20)	15 days	Mon 6/29/15	Fri 7/17/15	10
12	Install Ballustrades	25 days	Mon 7/20/15	Fri 8/21/15	11
13	Stucco Application	10 days	Mon 8/24/15	Fri 9/4/15	12
14	Dustwall repairs @ Unit #2214 / #2314	18 days	Mon 6/22/15	Wed 7/15/15	
15	Dustwall repairs @ Unit #714 / #814 / #914 / #1014	12 days	Thu 7/16/15	Fri 7/31/15	14
16	Dustwall repairs @ Unit #1814 / #1914	6 days	Mon 8/3/15	Mon 8/10/15	15
17	Dustwall repairs @ Unit #1214 / #1414 / #1514	9 days	Tue 8/11/15	Fri 8/21/15	16
18	Dustwall repairs @ Unit #214 / #314 / #414	9 days	Mon 8/24/15	Thu 9/3/15	17
19	Dustwall repairs @ Unit #1614	3 days	Fri 9/4/15	Tue 9/8/15	18
20	Dustwall repairs @ Unit #2414	3 days	Wed 9/9/15	Fri 9/11/15	19
21	Install SGD track @ Unit #1714	2 days	Mon 9/14/15	Tue 9/15/15	20
22	Spot Prime & Paint	5 days	Mon 9/7/15	Fri 9/11/15	13
23	Remove Swing Stage	2 days	Mon 9/14/15	Tue 9/15/15	20
24					
25	<b>Drop #4 (large balcony)</b>	<b>50 days</b>	<b>Mon 6/22/15</b>	<b>Fri 8/28/15</b>	
26	Assemble Swing Stage	2 days	Mon 6/22/15	Tue 6/23/15	
27	Remove Ballustrades	5 days	Wed 6/24/15	Tue 6/30/15	26
28	Demo: Concrete Slabs	8 days	Wed 7/1/15	Fri 7/10/15	27
29	Pour: Concrete Slabs	14 days	Mon 7/13/15	Thu 7/30/15	28
30	Install Ballustrades	9 days	Fri 7/31/15	Wed 8/12/15	29
31	Stucco Application	5 days	Thu 8/13/15	Wed 8/19/15	30
32	Spot Prime & Paint	3 days	Thu 8/20/15	Mon 8/24/15	31
33	Remove Swing Stage	2 days	Tue 8/25/15	Wed 8/26/15	32
34	Remove Overhead Protection	2 days	Thu 8/27/15	Fri 8/28/15	33

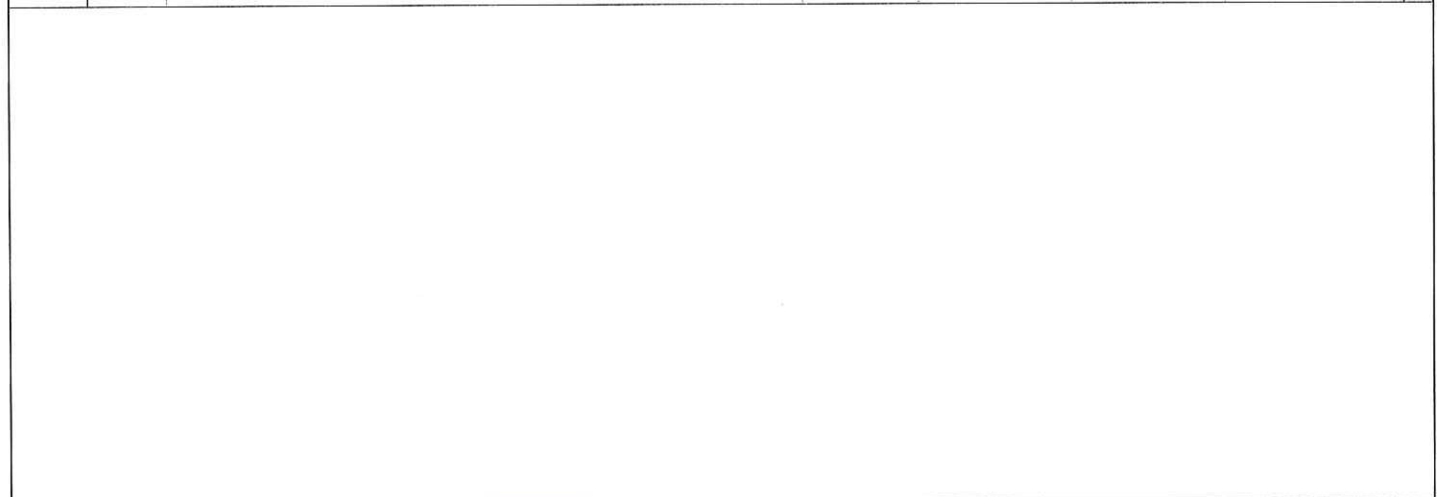

Project: HAMPTONS WEST Date: Tue 7/7/15	Task		Project Summary	
	Split		External Tasks	
	Progress		External Milestone	
	Milestone		Deadline	
	Summary			
